

Civil Works Transformation


SMART Feasibility Studies *Milestones & Process*




US Army Corps of Engineers
**PLANNING SMART
BUILDING STRONG®**



SMART Feasibility Study Process

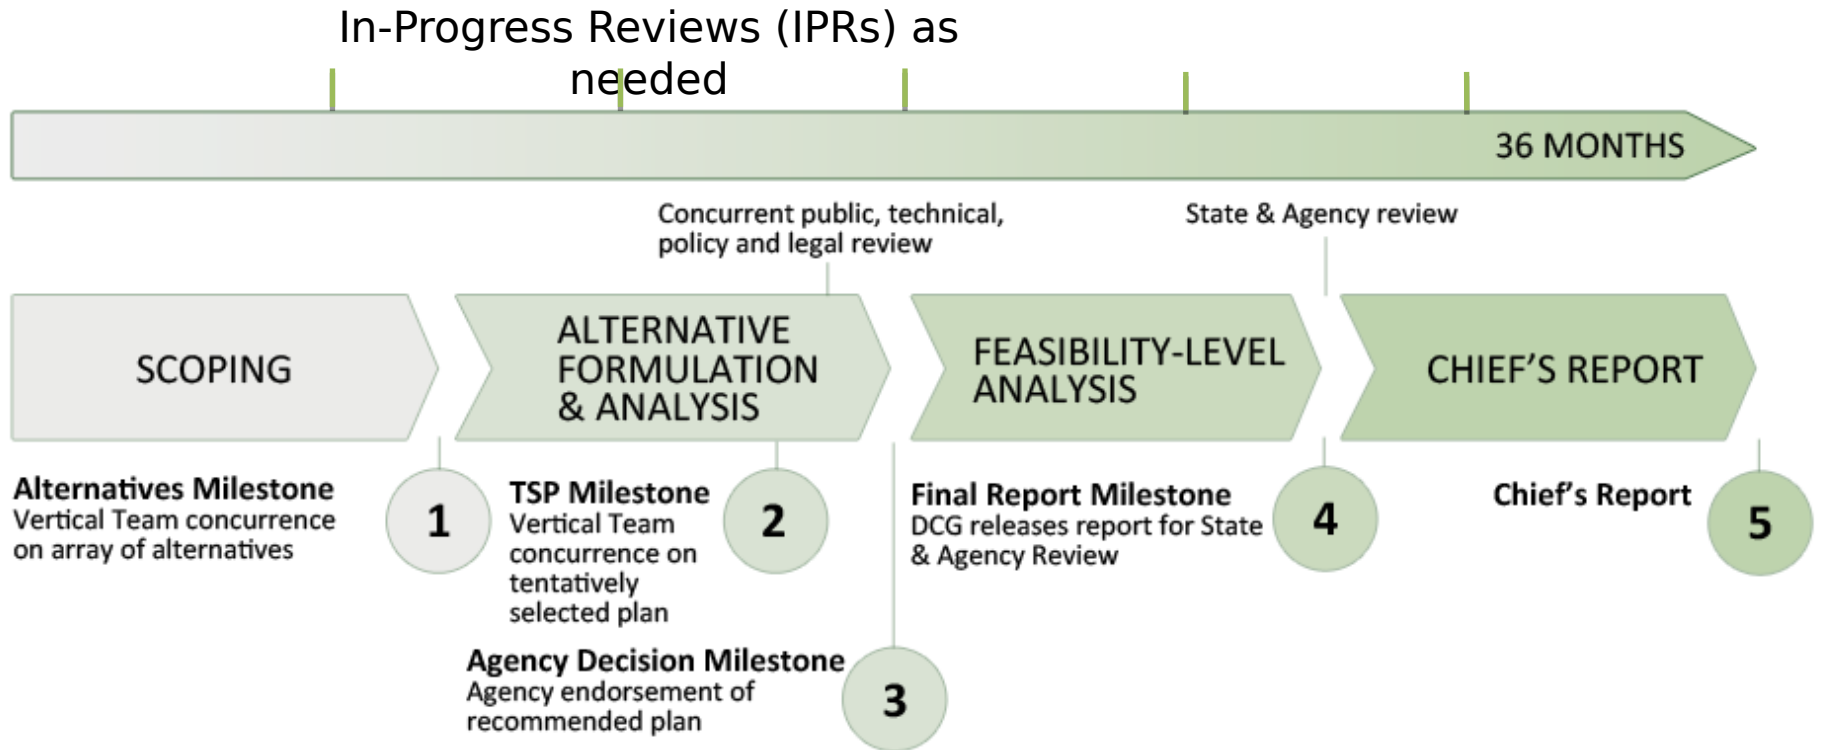

The Right Level of Detail at the Right Time

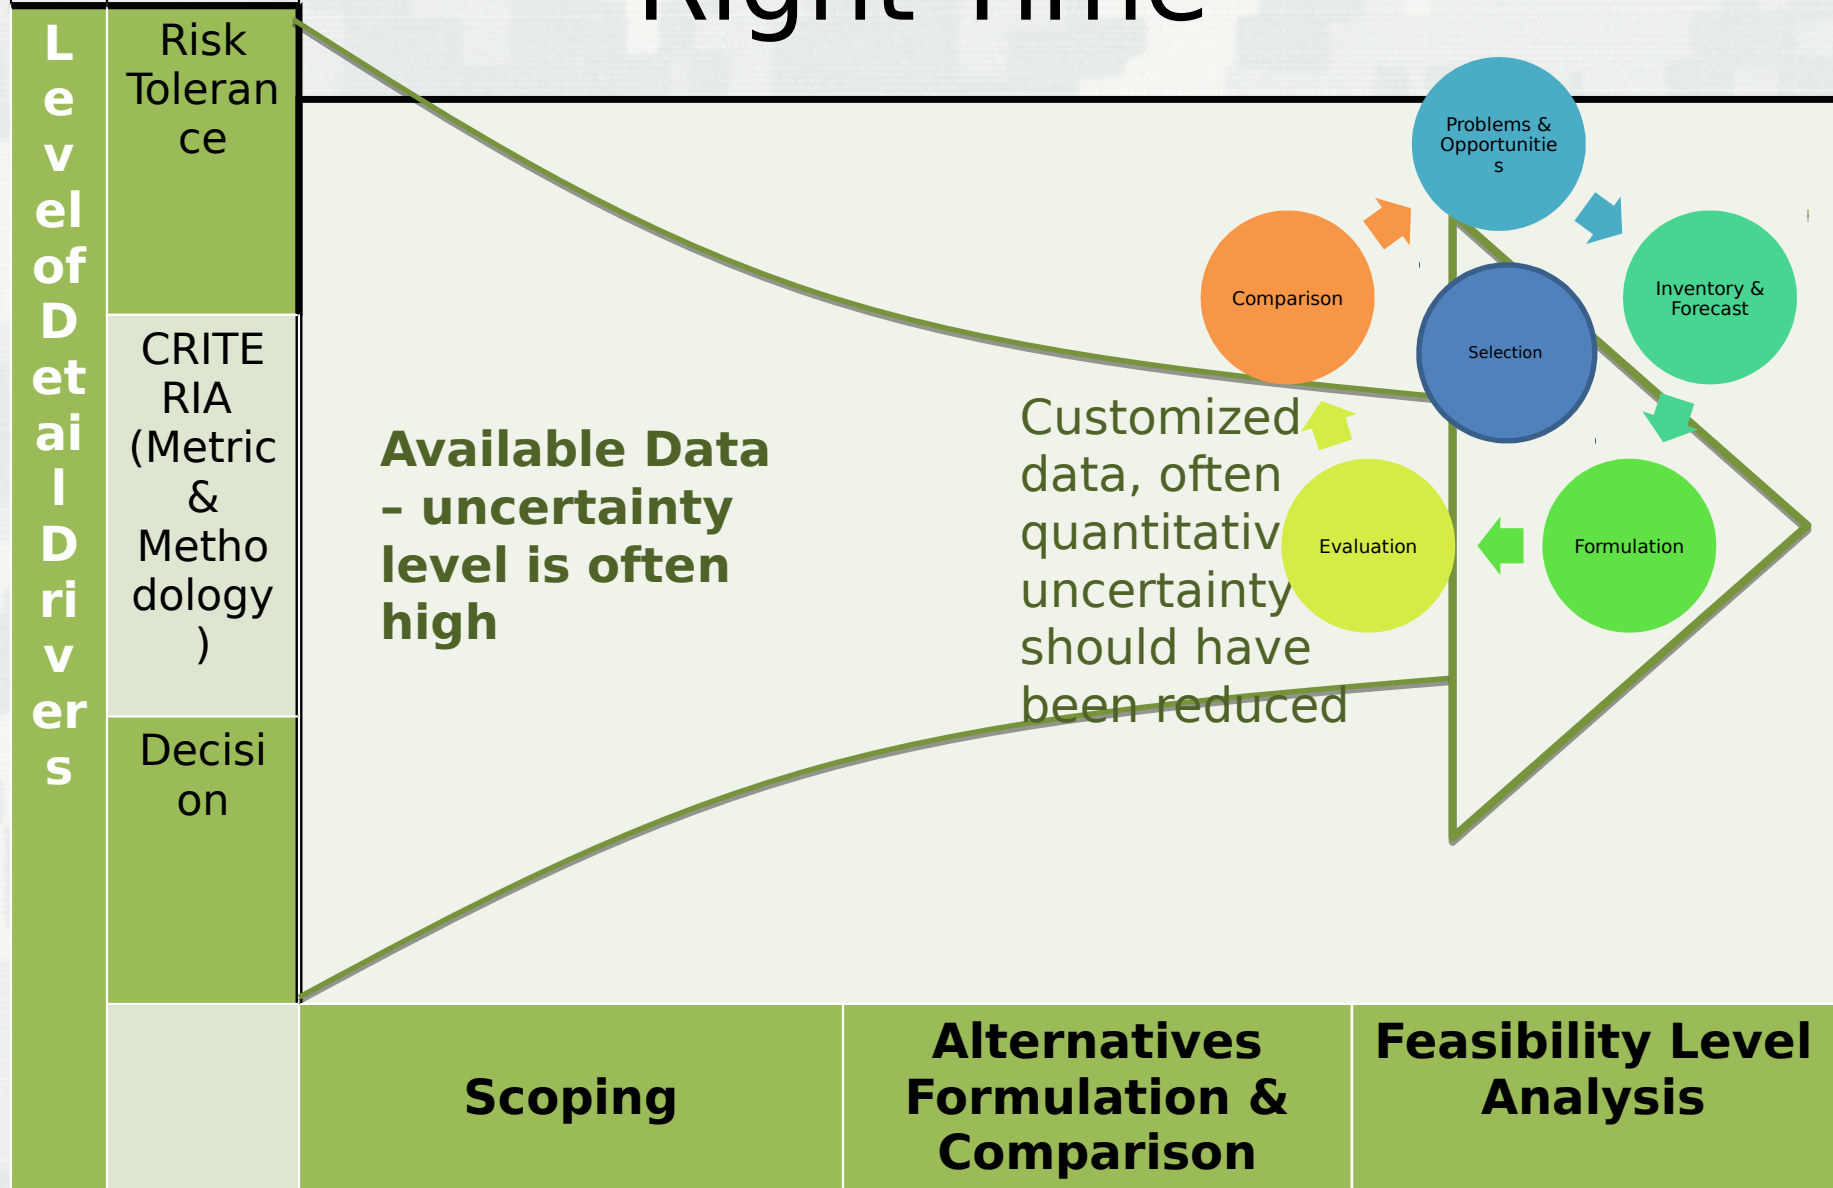

At Every Step

- Communicate with Vertical Team throughout process, not just at Milestones
- Document and share decisions made by PDT and Vertical Team
- Think critically – Can we make a decision with what we know now?



Tools for SMART Planning


- Planning Charette –intensive workshop bringing together Study Team and Vertical Team
- In Progress Reviews and other Team Meetings
- Decision Management Plan – maps path to the next major study decision
- Risk Register – documents study and project uncertainty / risk so it can be managed
- Decision Log
- Examples, Tips, Tools & Techniques on the Planning SMART Guide



Scoping → Alternatives Milestone

1. Encourage public and agency input and interaction. If EIS will be required, issue public NOI & scoping meeting.
2. Accelerate the process with a facilitated Planning Charette with PDT, Vertical Team, non-federal sponsors, USACE expertise appropriate to issues, and other key stakeholders.

d array of alternatives
tep planning process.



Scoping → Alternatives Milestone

4. **Alternatives Milestone:** VT confirms array of alternatives and the criteria the PDT will use for evaluation and comparison.

Report Synopsis

- Decisions to Date

Tools & Information

- Decision Management Plan
- Risk Register
- Decision Log
- Review plan



SCOPING

1


Alternatives Milestone
Vertical Team concurrence
on array of alternatives



BUILDING STRONG®

Alternatives Formulation & Analysis → TSP & Agency Decision Milestones

1. PDT uses the models / data needed to reduce unacceptable uncertainty in plan evaluation and comparison.
- 2. TSP Milestone:** VT confirms the tentatively selected plan recommended by the PDT.
3. Public Review: Draft feasibility report released, including evaluation analysis and draft recommendation.
4. Agency Review: ATR, IEPR (if needed). HQ Policy
Division's legal review



Alternatives Formulation & Analysis → TSP & Agency Decision Milestones

5. PDT updates draft feasibility report in response to public and agency review.


6. Agency Decision Milestone: Senior HQUSACE Leadership endorses recommended plan for feasibility-level design.

Draft Report

- Recommended Plan

Tools &
Information

- Risk Register
- Decision Management Plan
- Decision Log
- Review plan

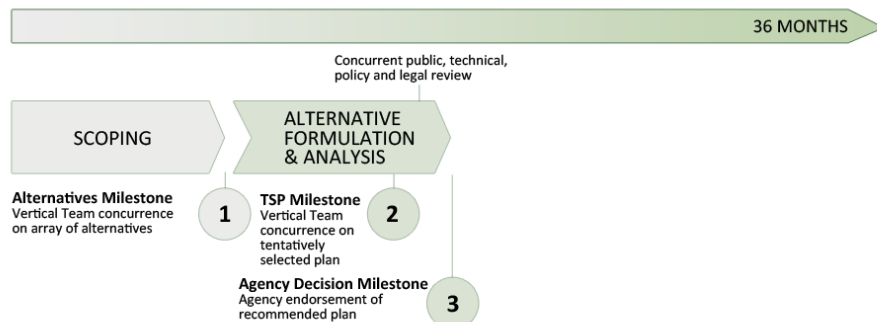


BUILDING STRONG®

Feasibility Level Analysis → Final Report Milestone

1. PDT addresses comments from HQUSACE Leadership and scales measures of the recommended alternative, reducing project and study uncertainty, completes the report.

2. Final Report Milestone: DCG-CEO briefed on recommendation and releases ~~Final Report for State~~ and Agency Review.

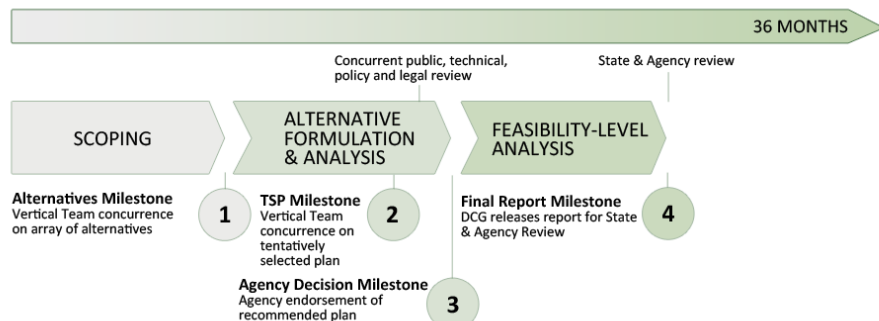

BUILDING STRONG®

Feasibility Level Analysis → Final Report Milestone


3. Division Engineer Notice of final recommendation.
4. Final EIS (or FONSI) published.

Feasibility Report

- Study
- Decisions to Date


Tools & Information

- Risk Register
- Decision Log
- Review plan

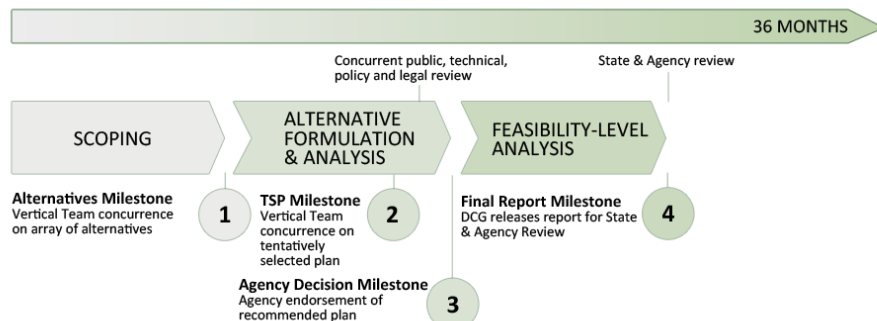

Final Feasibility Study Report → Chief's Report Milestone

1. PDT finalizes the feasibility study report, addressing state and agency comments.
2. Policy Review & Legal Certification.
3. Chief's Report prepared.
- 4. Chief's Report Milestone:** Chief signs the report.
5. Record of Decision prepared.

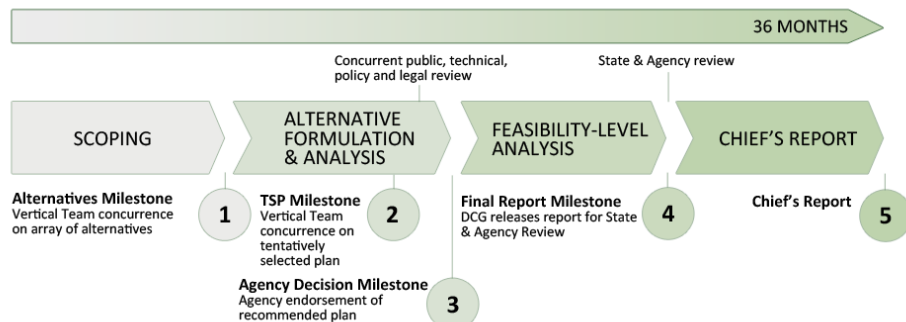

The Results

- “No Surprise” Reviews
- Increased Trust and Cooperation
- Studies completed in a more reasonable amount of time
- Studies cost significantly less
- High quality and concise decision documents
- Decisions informed by managing risk and acknowledging uncertainty
- Strong, viable Civil Works Project portfolio developed



Planning SMART Guide

Published online at www.corpsplanning.us – allows for timely content updates

- Feasibility Study Phases
 - Scoping
 - Alternative Formulation & Analysis
 - Feasibility-Level Design
 - Chief's Report
- SMART Planning Tips & Tools
 - Tips for Highly Effective Studies
 - Business Line Guides
 - Risk Register Template
 - Decision Log
 - Report Synopsis Example
 - 100-Page Report Example
- Review Primer
- And more!



BUILDING STRONG®
